

SUPPLY SCOPE (distributor quantities issue, no material prices): Nudura 6in XR35 external walls, GF + FF to the wall plate, ICF on the slab, plus the front gables - pre-cut by BuildEase, stock forms and accessories by the distributor. The slab, floors, steels, stairs, roof, partitions, windows, chimney and porch are DESIGN ASSUMPTIONS drawn in good faith for coordination only (England - Approved Documents) - engineer / specialists to design.

QUOTATION - NOT FOR CONSTRUCTION

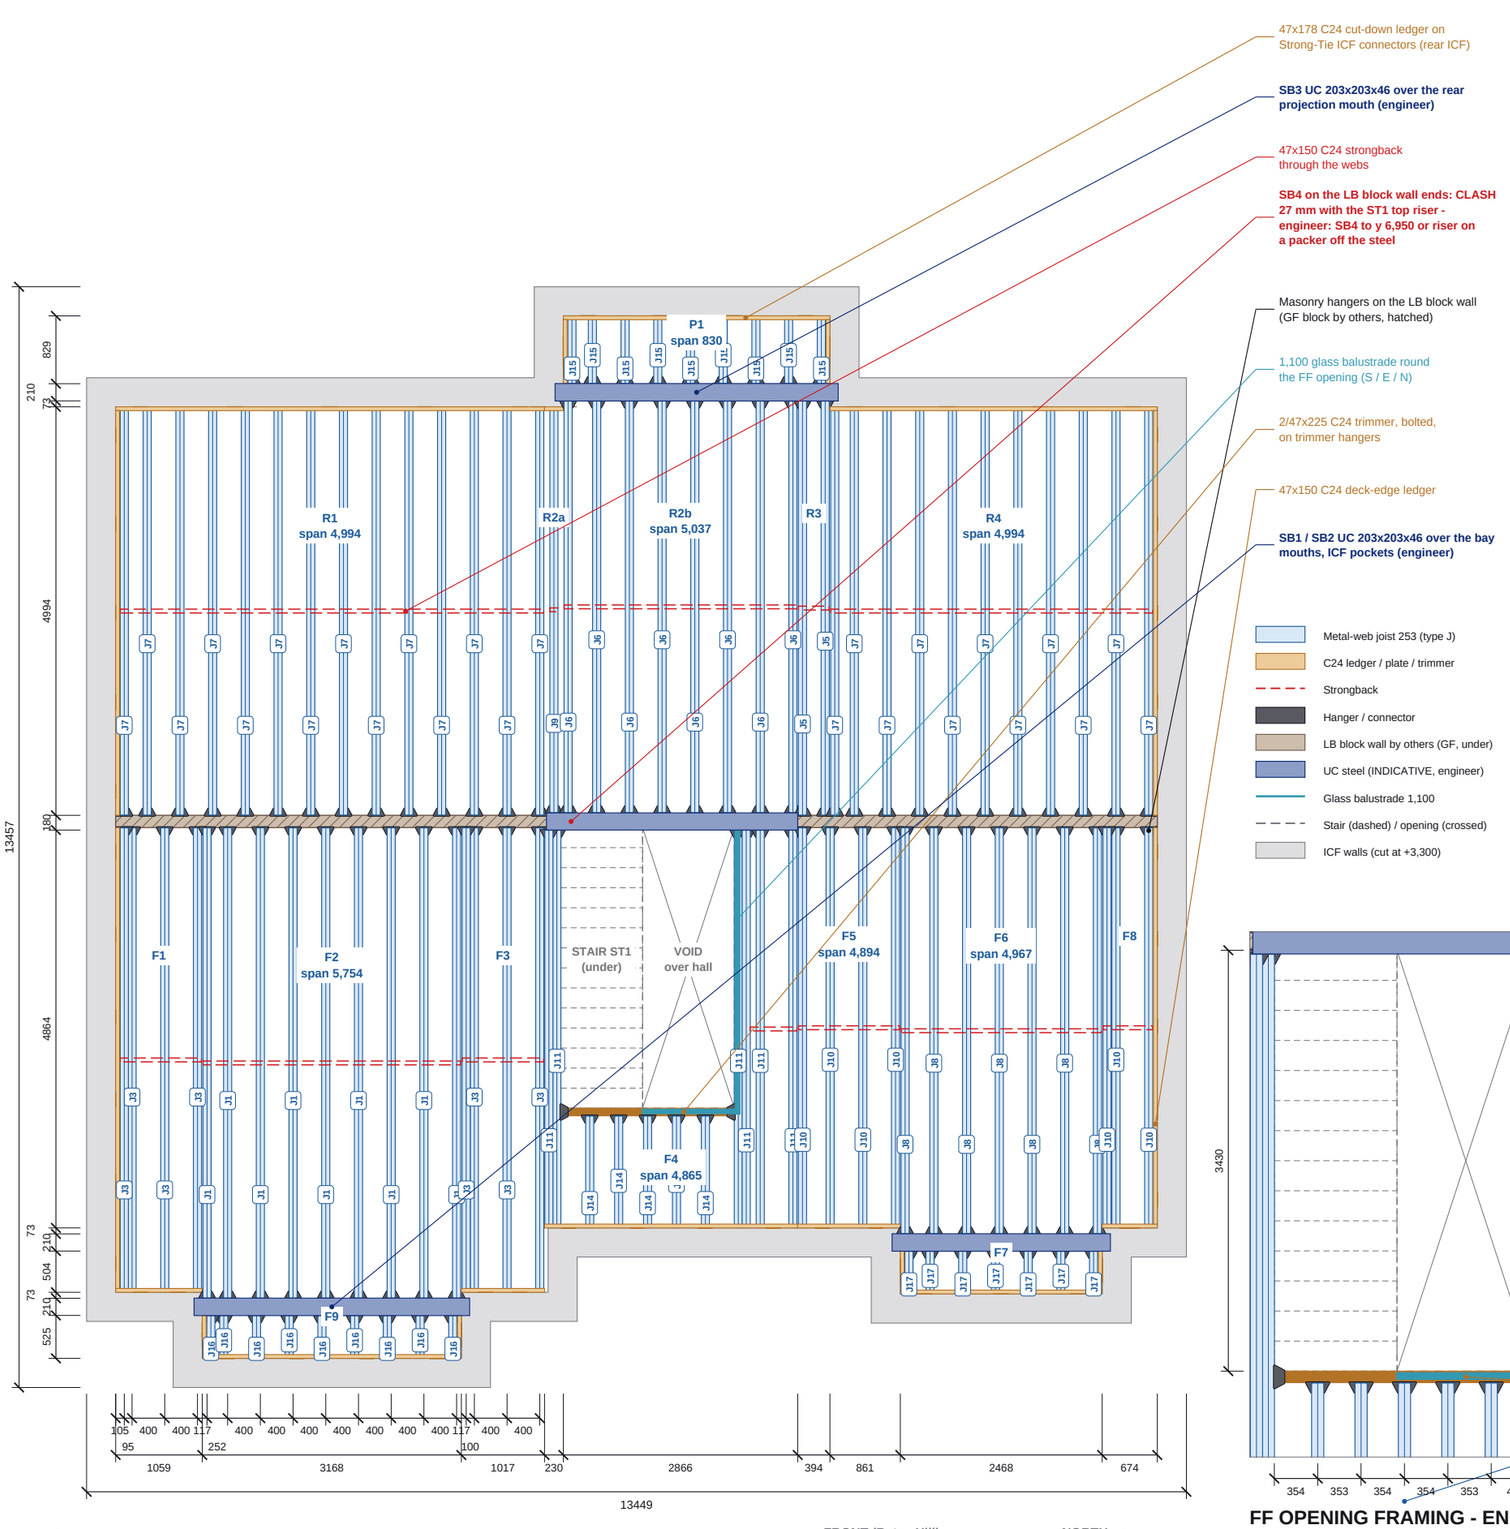

FIRST FLOOR JOIST LAYOUT

Scale 1:75 @ A3 | Plan on the joists, deck omitted

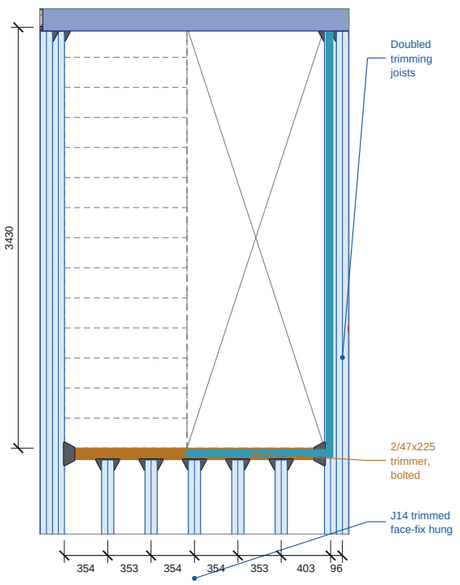

FF OPENING FRAMING - ENLARGED

Scale 1:50 | ST1 + hall void, trimming

FIRST FLOOR SCHEDULES

JOIST SCHEDULE (253 DEEP, @400)

Type	O/A	Bottom	Bearing	Bays	Qty
J1	5,748	5,748	hung both ends	F2	9
J3	5,675	5,628	top-hung + hung	F1, F3	8
J5	5,061	5,061	hung both ends	R3	2
J6	5,031	5,031	hung both ends	R2b	8
J7	4,988	4,941	top-hung + hung	R1, R4	25
J8	4,961	4,961	hung both ends	F6	7
J9	4,959	4,912	top-hung + hung	R2a	1
J10	4,888	4,841	top-hung + hung	F5, F8	7
J11	4,859	4,812	top-hung + hung	F4	6
J14	1,364	1,317	trimmed (hung)	F4	5
J15	824	777	top-hung + hung	P1	9
J16	519	472	top-hung + hung	F9	9
J17	518	471	top-hung + hung	F7	7
	Total				**103**

O/A = top flange overall; Bottom = bottom flange. Includes 4 No. in doubled (bolted) pairs. Types common to both floors; profiles on ES26-075-FL-03.

LEDGERS, STRONGBACKS, TRIMMERS, BINDERS (C24)

Item	Length	Qty	Run m
2/47x225 trimmer, bolted	2,116	1	2.1
47x150 deck-edge ledger	477-5,634	10	23.9
47x150 strongback	97-5,177	12	22.4
47x178 ledger cut-down	230-5,244	11	25.5

METALWORK, DECK AND GUARDING

Item	Qty
Top-chord restraint clip (galv)	77
Strong-Tie ICFVL-CW + ICFLC ICF connector	67
Masonry joist hanger (block walls)	58
Face-fix hanger on timber packer in UC web	66
Face-fix trimmer hanger	2
Face-fix joist hanger off trimmer	5
22 Egger Protect P5 T&G board	204 (132.9 m2)
Glass balustrade 1,100 + base shoe + cap rail (3 runs)	5.9 m

FF STEELS (INDICATIVE - ENGINEER)

Mark	Section	Line	Bearing	Length	kg
SB1	UC 203x203x46 S355	y 986	ICF	3,370	155
SB2	UC 203x203x46 S355	y 1,773	ICF	2,670	123
SB3	UC 203x203x46 S355	y 12,167	ICF	3,462	160
SB4	UC 203x203x46 S355	y 6,920	block	3,072	142
	Total (indicative)				**580**

NOTES

1. FF FFL +3,075: 253 metal-web joists (PS10 equiv., 97x47 C24 flanges) @400 spanning FRONT-REAR (y). ICF ends TOP-HUNG on 47x178 C24 cut-down ledgers; LB block wall ends on masonry hangers (block by others); steel ends on face-fix hangers to timber packers in the UC web.
2. Ledgers on cast-in Strong-Tie ICFVL-CW + ICFLC, ledger top +3,006, joist top +3,053. Deck-edge ledgers, strongbacks at mid-span > 4 m, 22 Egger P5 deck.
3. FF OPENING x 5,799-7,921 / y 3,415-6,845: doubled trimming joists, 2/47x225 trimmer, trimmed joists hung; 1,100 glass guard. ST1 15 x 205 / 245, headroom 2,549.
4. STEELS INDICATIVE - engineer. CLASH: SB4 flange tip y 6,818 is 27 mm inside the ST1 top riser y 6,845: SB4 to y 6,950 or riser on a packer (engineer). Joist supplier to design; pricing only.

REVISIONS

REV	DATE	DESCRIPTION
-	02.11.26	Quotation issue

Nudura™ BuildEase

CLIENT	PROJECT
ICF Supplies Ltd (distributor) - Tom Barrett	Plot 1, The Rectory, Bates Hill, Ightham TN15 9BG

DRAWING TITLE

FIRST FLOOR STRUCTURE

Metal-web joists, ledgers, hangers, strongbacks, FF opening trimming, FF steels

SCALE	SIZE	DATE
AS SHOWN	A3	02.11.26
DRAWN	CHECKED	APPROVED
TS		

STATUS	DRAWING No.	REV
QUOTATION	ES26-075-FL-01	-

Do not scale. All dimensions in mm. Check all dimensions on site.
