
SUPPLY SCOPE (distributor quantities issue, no material prices): Nudura 6in XR35 external walls, GF + FF to the wall plate, ICF on the slab, plus the front gables - pre-cut by BuildEase, stock forms and accessories by the distributor. The slab, floors, steels, stairs, roof, partitions, windows, chimney and porch are DESIGN ASSUMPTIONS drawn in good faith for coordination only (England - Approved Documents) - engineer / specialists to design.

QUOTATION - NOT FOR CONSTRUCTION


J3 - 5,675 O/A x 253 - 8 No.

TOP-HUNG on the ICF ledger one end, HUNG (block / steel) the other (same bearing: J7, J9, J10, J11, J15, J16, J17)




J1 - 5,748 O/A x 253 - 9 No.

HUNG BOTH ENDS (masonry hangers / face-fix on the steel packers) (same bearing: J5, J6, J8)




J14 - 1,364 O/A x 253 - 5 No.

TRIMMED: face-fix hung off the opening trimmer, ICF ledger the other end




J2 - 5,688 O/A x 253 - 4 No.

BOTTOM-BEARING on the 150 wall plate / LB stud wall head (truss clips) - SF (same bearing: J4, J12, J13)



Elevations 1:25 - ledger / ICF (grey), hanger + block or steel support (hatched), wall plate / stud head (timber) shown at each end for context

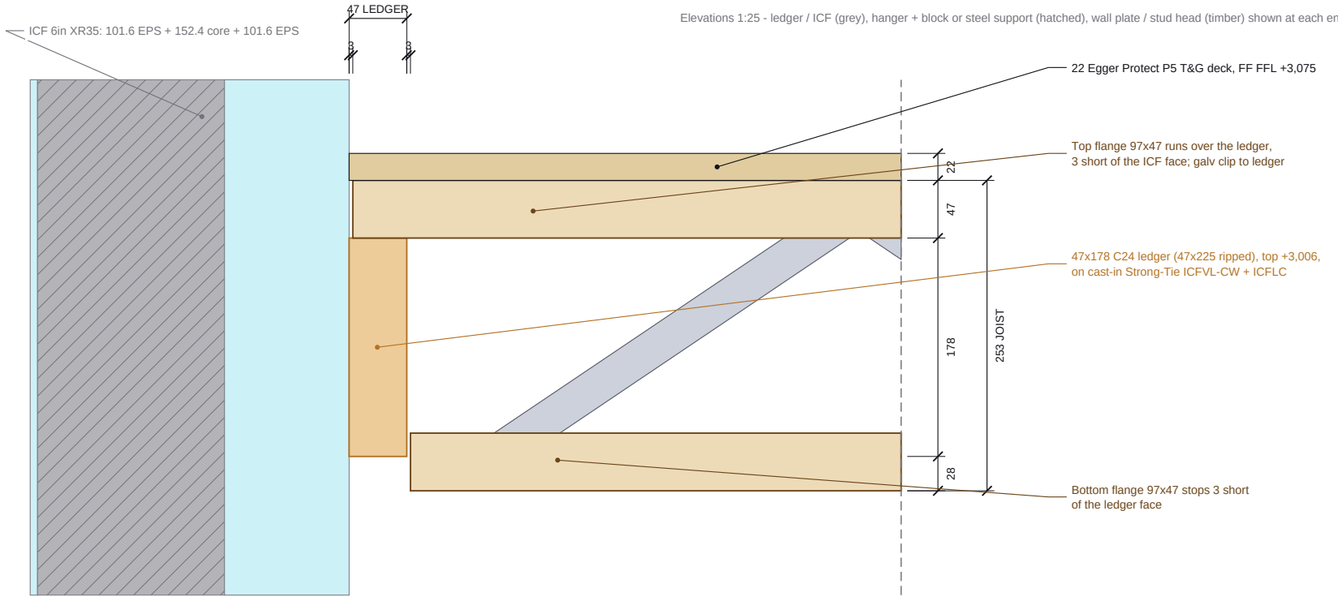

TOP-HUNG BEARING ON CUT-DOWN LEDGER

Scale 1:5 | typical ICF end, FF (SF +5,911 bears on plates / stud heads)

JOIST TYPES

JOIST SCHEDULE (253 DEEP, 97X47 FLANGES)

Type	O/A	Bottom	Bearing	FF	SF	Qty
J1	5,748	5,748	hung both ends	9	0	9
J2	5,688	5,688	bottom-bearing	0	4	4
J3	5,675	5,628	top-hung + hung	8	0	8
J4	5,563	5,563	bottom-bearing	0	26	26
J5	5,061	5,061	hung both ends	2	0	2
J6	5,031	5,031	hung both ends	8	0	8
J7	4,988	4,941	top-hung + hung	25	0	25
J8	4,961	4,961	hung both ends	7	0	7
J9	4,959	4,912	top-hung + hung	1	0	1
J10	4,888	4,841	top-hung + hung	7	0	7
J11	4,859	4,812	top-hung + hung	6	0	6
J12	3,462	3,462	bottom-bearing	0	20	20
J13	1,811	1,811	bottom-bearing	0	27	27
J14	1,364	1,317	trimmed (hung)	5	0	5
J15	824	777	top-hung + hung	9	0	9
J16	519	472	top-hung + hung	9	0	9
J17	518	471	top-hung + hung	7	0	7
			Total	**103**	**77**	**180**

Qty includes the doubled (bolted) edge / trimming pairs. Layouts on ES26-075-FL-01 (first floor) and ES26-075-FL-02 (second floor).

WHERE USED (BAYS)

Type	Bays (FF F/R/P, SF S)
J1	F2
J2	S0
J3	F1, F3
J4	S1
J5	R3
J6	R2b
J7	R1, R4
J8	F6
J9	R2a
J10	F5, F8
J11	F4
J12	S2a, S2b
J13	S3
J14	F4
J15	P1
J16	F9
J17	F7

NOTES

1. FOR SUPPLIER QUOTE: 253 deep metal-web joists, e.g. Posi-Joist / Easi-Joist PS10 equivalent, 97x47 C24 (or stress-graded) flanges with galvanised V-web plates. The supplier designs the joists for the stated loads and confirms depth, web layout, spacing, hangers and bracing. Web pattern shown indicative.
2. Loads (to be confirmed by the supplier, Approved Document A / BS EN 1991): FF + SF domestic, imposed 1.5 kN/m2 + lightweight stud partitions over; 22 Egger Protect P5 deck, plasterboard ceiling under. 400 c/c.
3. FF: top-hung bearing at the ICF - top flange over the 47x178 C24 ledger to 3 short of the ICF face; bottom flange stops 3 short of the ledger; galv restraint clip to the ledger. LB block wall ends: masonry hangers built in (blockwork by others). Steel ends (SB1-SB4): face-fix hangers on timber packers bolted in the UC web.
4. SF: bottom-bearing on the 150 wall plates and the LB stud wall heads (FF-P02 / P05 / P09), galv truss clips.

REVISIONS

REV	DATE	DESCRIPTION
-	02.11.26	Quotation issue

Nudura™ BuildEase

CLIENT	PROJECT
ICF Supplies Ltd (distributor) - Tom Barrett	Plot 1, The Rectory, Bates Hill, Ightham TN15 9BG

DRAWING TITLE

FLOOR JOIST PROFILES

Metal-web joist profiles for supplier quotation

SCALE	SIZE	DATE
1:25 / 1:5	A3	02.11.26
DRAWN	**CHECKED**	**APPROVED**
TS		

STATUS	DRAWING No.	REV
QUOTATION	ES26-075-FL-03	-

Do not scale. All dimensions in mm. Check all dimensions on site.
