
SUPPLY SCOPE (distributor quantities issue, no material prices): Nudura 6in XR35 external walls, GF + FF to the wall plate, ICF on the slab, plus the front gables - pre-cut by BuildEase, stock forms and accessories by the distributor. The slab, floors, steels, stairs, roof, partitions, windows, chimney and porch are DESIGN ASSUMPTIONS drawn in good faith for coordination only (England - Approved Documents) - engineer / specialists to design.

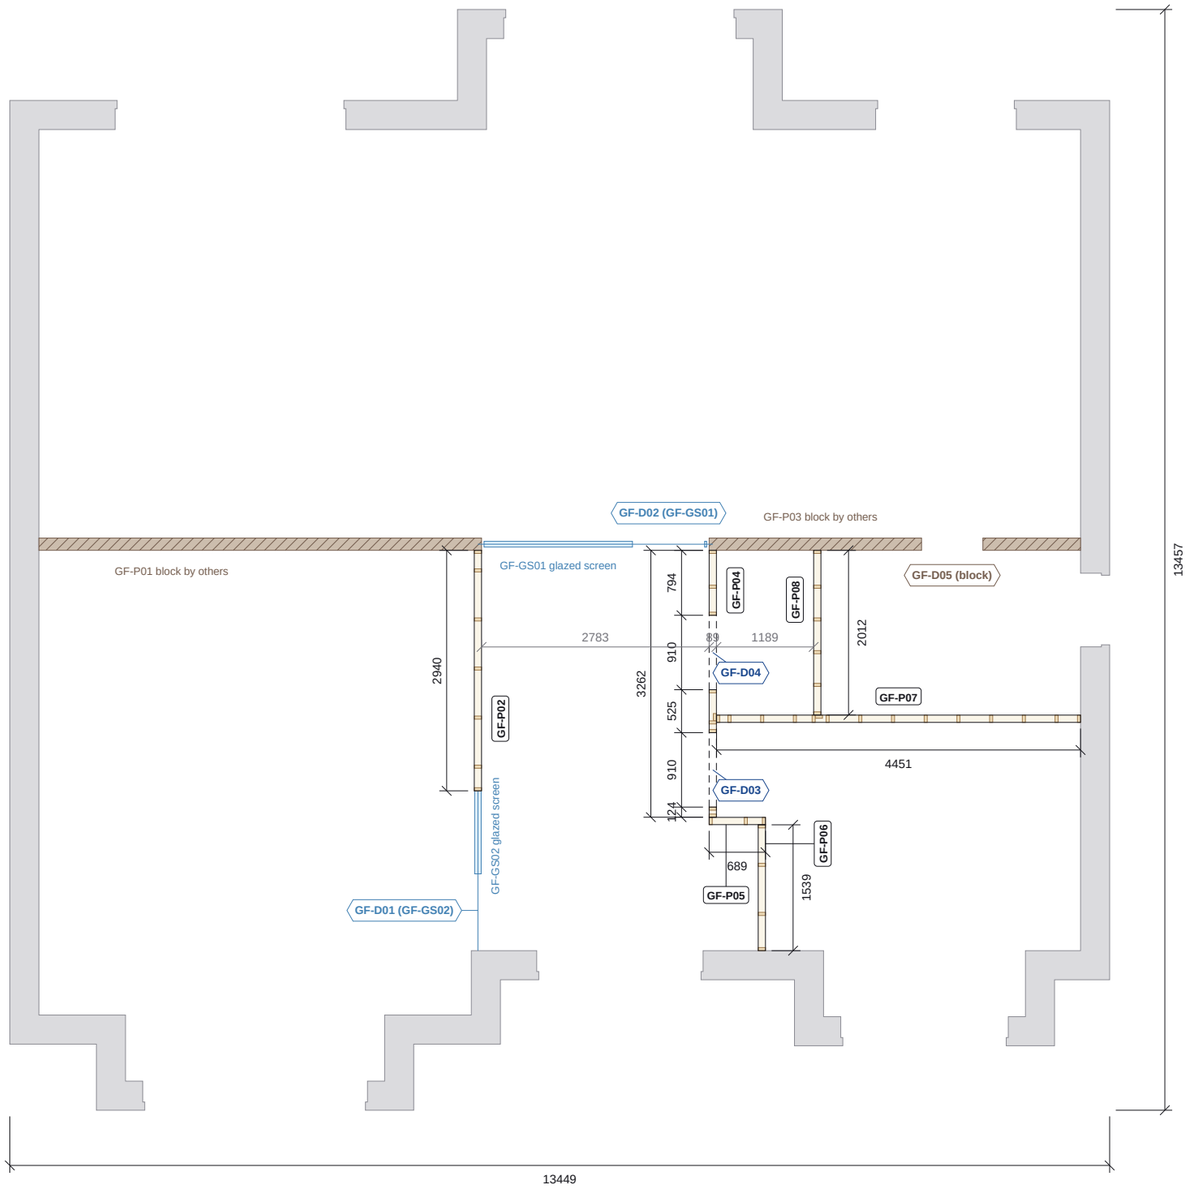

GROUND FLOOR TIMBER PARTITIONS PLAN

Scale 1:75 @ A3 | Plan cut at 1000 above GF FFL +0

0 1 2 3 4 5m

Partition panel, studs cut | Panel joint | Nudura ICF (context only) | Door opening, head over | Block wall by others | Glazed screen (joinery)

QUOTATION - NOT FOR CONSTRUCTION

GROUND FLOOR SCHEDULES

PARTITION SCHEDULE

Panel	Head	C16 studs	Use	Length	Doors
GF-P02	2,795	38x89 @600	partition	2940	-
GF-P04	2,795	38x89 @400	wet room	3262	GF-D03, GF-D04
GF-P05	2,795	38x89 @600	partition	689	-
GF-P06	2,795	38x89 @600	partition	1539	-
GF-P07	2,795	38x89 @400	wet room	4451	-
GF-P08	2,795	38x89 @400	wet room	2012	-

Length along the wall (mm). Head = top of frame above GF FFL, 5 under the FF joist underside +2,800.

DOOR OPENING SCHEDULE

Label	Width	Height	Head	Lintel
GF-D03	910	2100	2100	head rail
GF-D04	910	2100	2100	head rail

Structural opening sizes. Head level above underside of the bottom rail. GF-D01 / D02 (glazed screens) and GF-D05 (block wall) are by others.

PARTITION TIMBER (GROUND FLOOR)

Section	Pieces	Run m	4.8m lengths
38x89 C16	104	167.6	37
18 WBP ply pattress	50	-	-
Slotted partition head clip	40	-	-
47x97 C24 head noggin	4	-	-

From the model. 4.8m lengths = run / 4.8 +5%, not cut-optimised.

NOTES

1. DESIGN ASSUMPTION - internal partitions (TLSTF) read off Offset 9172-SK10 (preliminary): 38x89 C16 studs @600, 38x89 head and bottom rails, 15 plasterboard each side (119); wet-room walls (WC, utility) at 400 centres with 18 WBP ply pattress in the stud bays, 150-1950 above floor (50 pieces).
2. External walls Nudura 6in XR35 ICF (grey), context only - read with the ICF GAs. GF-P01 / GF-P03 are 150 dense BLOCK load-bearing walls BY OTHERS (hatched brown, coordination only); glazed screens GF-GS01 / GF-GS02 with doors GF-D01 / GF-D02 are joinery (blue outline). Set-out strings in grey.
3. Non-load-bearing: heads stop 5 short of the FF PS10 metal-web joist underside (+2,800; frame top +2,795), restrained with galv slotted partition head clips to the joist bottom chords / 47x97 C24 noggins (40 No. clips, 4 noggins where a partition runs parallel to the joists, 5 mm deflection gap) - clip product to confirm. Joist designer to confirm.
4. Sole plates fixed to the GF slab at <= 600 c/c, DPC under. Door openings are structural opening sizes; door heads 2,100 on the head rail. Dimensions to timber frame faces; check all dimensions on site.

REVISIONS

REV	DATE	DESCRIPTION
-	02.11.26	Quotation issue

Nudura™ BuildEase

CLIENT	PROJECT
ICF Supplies Ltd (distributor) - Tom Barrett	Plot 1, The Rectory, Bates Hill, Ightham TN15 9BG

DRAWING TITLE

GROUND FLOOR TIMBER PARTITIONS

Internal stud partitions, panels and door openings

SCALE	SIZE	DATE
1:75	A3	02.11.26
DRAWN	CHECKED	APPROVED
TS		

STATUS	DRAWING No.	REV
QUOTATION	ES26-075-TF-01	-

Do not scale. All dimensions in mm. Check all dimensions on site.
