
SUPPLY SCOPE (distributor quantities issue, no material prices): Nudura 6in XR35 external walls, GF + FF to the wall plate, ICF on the slab, plus the front gables - pre-cut by BuildEase, stock forms and accessories by the distributor. The slab, floors, steels, stairs, roof, partitions, windows, chimney and porch are DESIGN ASSUMPTIONS drawn in good faith for coordination only (England - Approved Documents) - engineer / specialists to design.

PARTITION TIMBER (FIRST FLOOR)

Section	Pieces	Run m	4.8m lengths
47x195 C24	5	4.6	2
45x195 C24	10	9.2	3
38x89 C16	155	244.4	54
38x140 C16	101	179.9	40
18 WBP ply pattress	69	-	-
Slotted partition head clip	42	-	-
47x97 C24 head noggin	6	-	-

From the model. 4.8m lengths = run / 4.8 +5%, not cut-optimised.

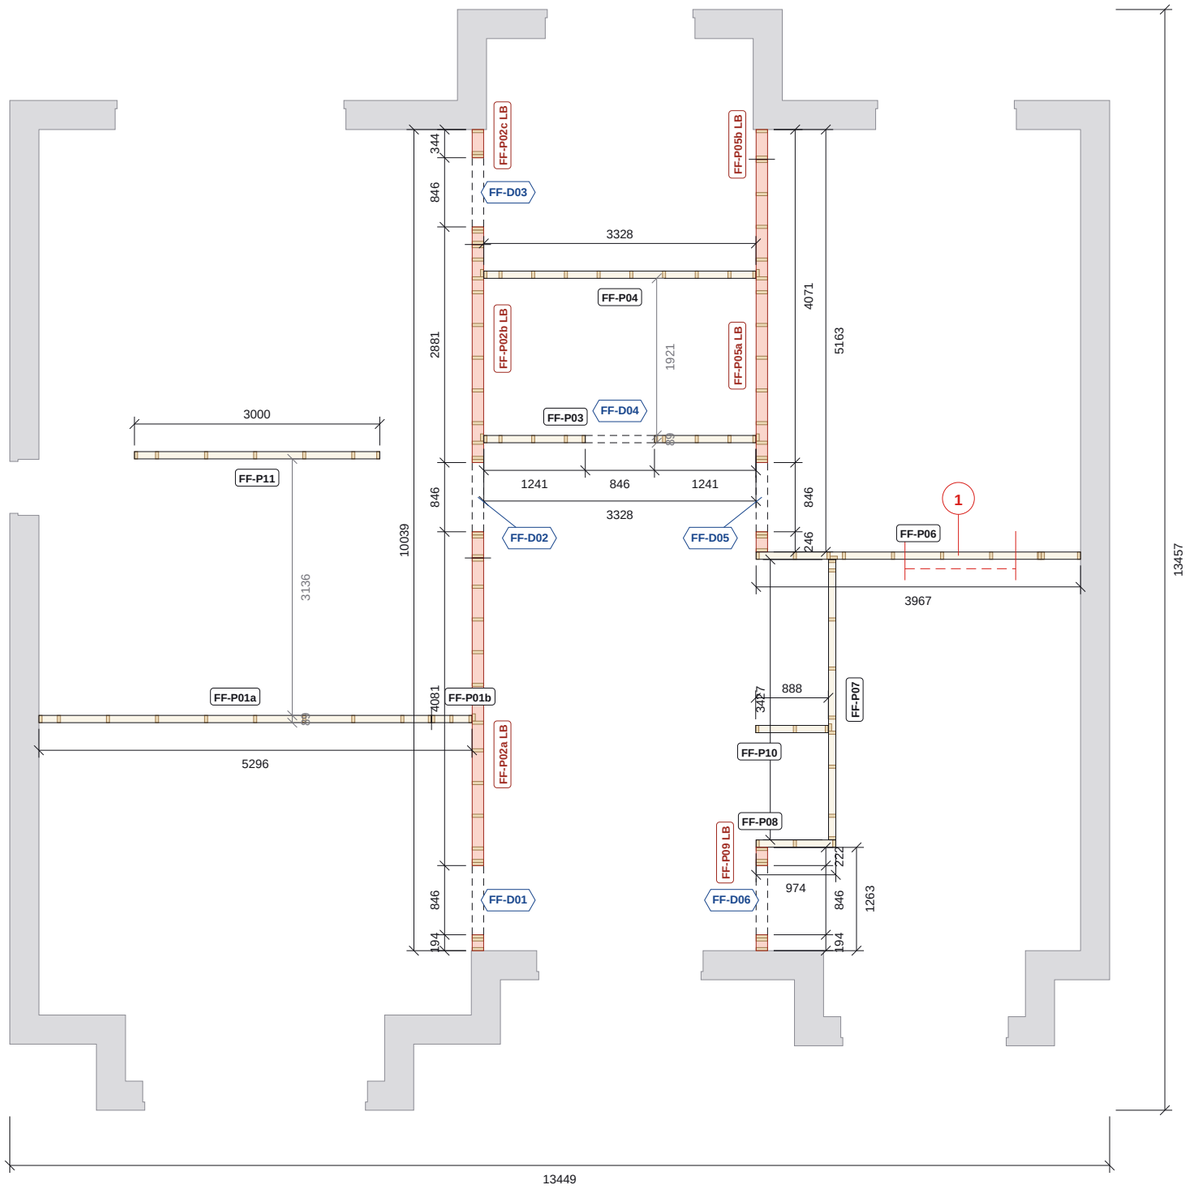

FIRST FLOOR TIMBER PARTITIONS PLAN

Scale 1:75 @ A3 | Plan cut at 1000 above FF FFL +3,075

0 1 2 3 4 5m

Partition panel, studs cut | Panel joint | Nudura ICF (context only) | Door opening, head over | LB stud wall - engineer | Open item - see notes

QUOTATION - NOT FOR CONSTRUCTION

Do not scale. All dimensions in mm. Check all dimensions on site.

FIRST FLOOR SCHEDULES

PARTITION SCHEDULE

Panel	Head	C16 studs	Use	Length	Doors
FF-P01a	5,631	38x89 @600	partition	4800	-
FF-P01b	5,631	38x89 @600	partition	494	-
FF-P02a	5,636	38x140 @400	LB - engineer	4800	FF-D01
FF-P02b	5,636	38x140 @400	LB - engineer	3830	FF-D02
FF-P02c	5,636	38x140 @400	LB - engineer	1404	FF-D03
FF-P03	5,631	38x89 @400	wet room	3328	FF-D04
FF-P04	5,631	38x89 @400	wet room	3328	-
FF-P05a	5,636	38x140 @400	LB - engineer	4798	FF-D05
FF-P05b	5,636	38x140 @400	LB - engineer	363	-
FF-P06	5,144-5,631 rk	38x89 @600	partition, E end rk	3967	-
FF-P07	5,631	38x89 @600	partition	3427	-
FF-P08	5,631	38x89 @600	partition	974	-
FF-P09	5,636	38x140 @400	LB - engineer	1263	FF-D06
FF-P10	5,631	38x89 @600	partition	888	-
FF-P11	4,170 (1,100)	38x89 @600	half-ht screen	3000	-

Length along the wall (mm). Head = top of frame above GF FFL: 5 under the SF joist underside +5,636; LB walls to it (joists bear); FF-P11 half-height 1,100; rk = raked min-max.

DOOR OPENING SCHEDULE

Label	Width	Height	Head	Lintel
FF-D01	846	2100	2100	2/45x195 C24 LB
FF-D02	846	2100	2100	2/45x195 C24 LB
FF-D03	846	2100	2100	2/45x195 C24 LB
FF-D04	846	2100	2100	head rail
FF-D05	846	2100	2100	2/45x195 C24 LB
FF-D06	846	2100	2100	2/45x195 C24 LB

Structural opening sizes. Head level above underside of the bottom rail. LB = lintel in a load-bearing wall - engineer to confirm.

NOTES

1. DESIGN ASSUMPTION - internal partitions (TLSTF) read off Offset 9172-SK10 (preliminary): 38x89 C16 studs @600, 38x89 head and bottom rails, 15 plasterboard each side (119); wet-room walls (bathroom, principal ensuite) at 400 centres with 18 WBP ply pattress in the stud bays, 150-1950 above floor (69 pieces).
2. External walls Nudura 6in XR35 ICF (grey), context only - read with the ICF GAs. Set-out strings in grey.
3. FF-P02 / FF-P05 / FF-P09 (red) are LOAD-BEARING - they carry the SF PS10 floor joists (joists bear on the head, 0 gap, galv truss clips): 38x140 C16 studs @400, 38x140 rails, 2/45x195 C24 lintels over their doors (FF-D01/D02/D03/D05/D06) - LB - ENGINEER to design and confirm the load path down to the foundations.
4. Non-load-bearing: heads stop 5 short of the SF joist underside (+5,636; frame top +5,631), galv slotted head clips to the joist bottom chords / noggins; FF-P06 east end raked under the north roof slope, clipped to the rafters (25 lining gap). 42 No. clips, 6 noggins. FF-P11 is a half-height 1,100 bed-head screen, free standing: braced base / post fixed through the deck to the joists.
5. Sole plates fixed through the FF deck (22 Egger Protect P5) to the PS10 joists / noggins at <= 600 c/c. Door openings are structural opening sizes. Dimensions to timber frame faces; check on site.
6. OPEN ITEM 1 (red flag): FF-P06 east end: NO head fixing between x 10,946 and ~12,300 - no SF joist over it (parallel, outside the joisted run) and the rafter clips only start at x 12,314. Add a ladder / noggins off the roof or SF trimmer - RFI / engineer.

REVISIONS

REV	DATE	DESCRIPTION
-	02.11.26	Quotation issue

Nudura™ BuildEase

CLIENT	PROJECT
ICF Supplies Ltd (distributor) - Tom Barrett	Plot 1, The Rectory, Bates Hill, Ightham TN15 9BG

DRAWING TITLE

FIRST FLOOR TIMBER PARTITIONS

Internal stud partitions, panels and door openings

SCALE	SIZE	DATE
1:75	A3	02.11.26
DRAWN	CHECKED	APPROVED
TS		

STATUS	DRAWING No.	REV
QUOTATION	ES26-075-TF-02	-
