
SUPPLY SCOPE (distributor quantities issue, no material prices): Nudura 6in XR35 external walls, GF + FF to the wall plate, ICF on the slab, plus the front gables - pre-cut by BuildEase, stock forms and accessories by the distributor. The slab, floors, steels, stairs, roof, partitions, windows, chimney and porch are DESIGN ASSUMPTIONS drawn in good faith for coordination only (England - Approved Documents) - engineer / specialists to design.

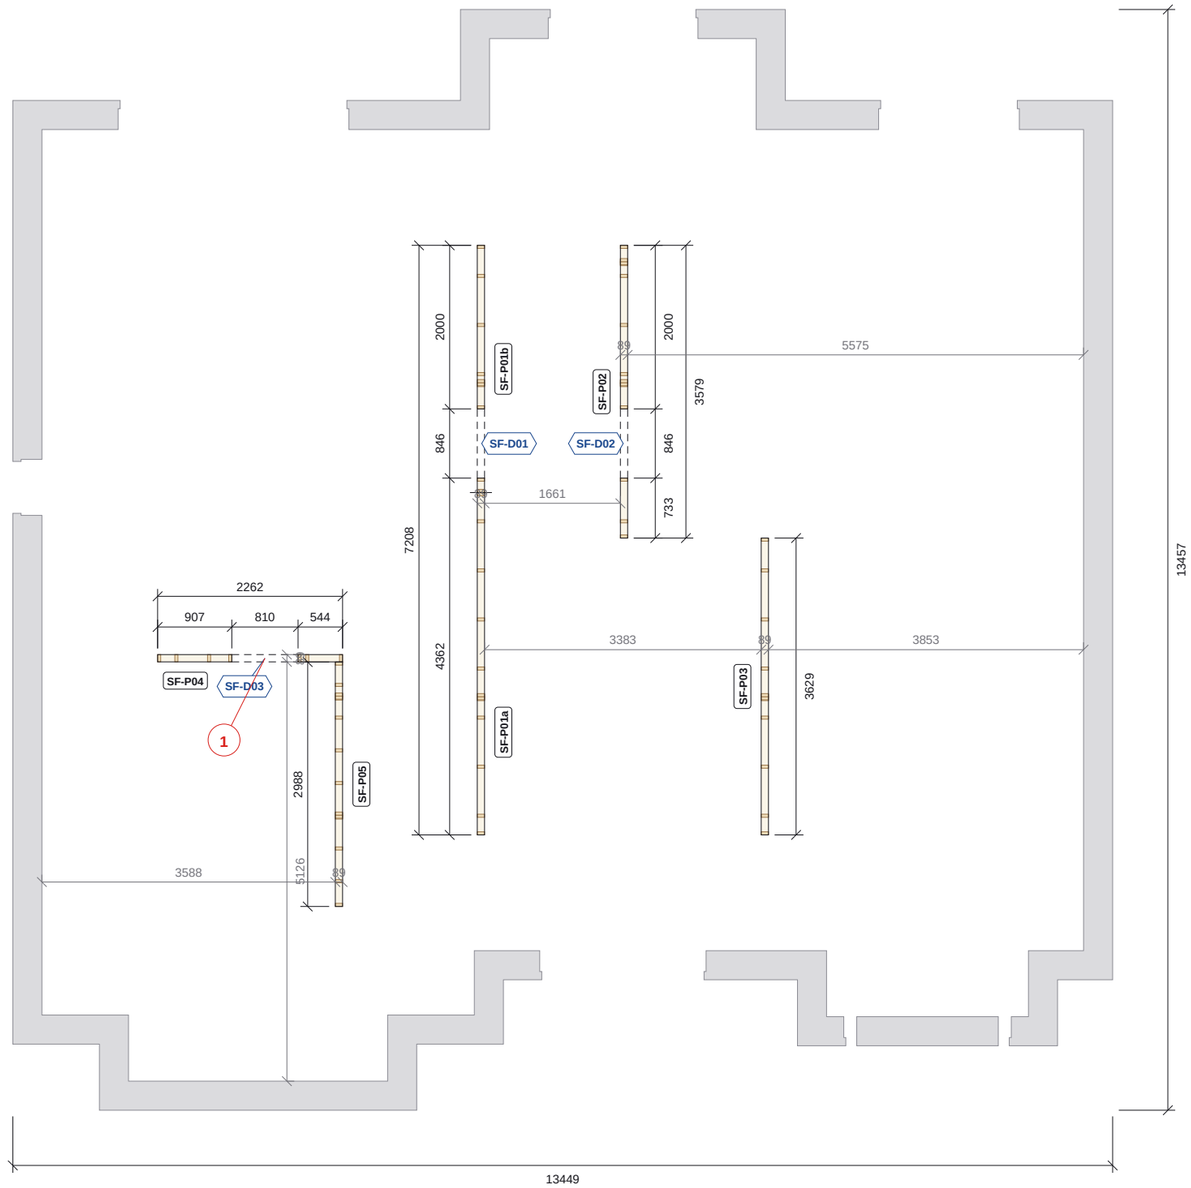

SECOND FLOOR TIMBER PARTITIONS PLAN

Scale 1:75 @ A3 | Plan cut at 1000 above SF FFL +5,911

0 1 2 3 4 5m

Partition panel, studs cut | Panel joint | Nudura ICF (context only) | Door opening, head over | Open item - see notes

QUOTATION - NOT FOR CONSTRUCTION

Do not scale. All dimensions in mm. Check all dimensions on site.

SECOND FLOOR (ROOM IN ROOF) SCHEDULES

PARTITION SCHEDULE

Panel	Head	C16 studs	Use	Length	Doors
SF-P01a	7,233-8,921 rk	38x89 @600	partition	4184	-
SF-P01b	7,233-8,921 rk	38x89 @600	partition	3022	SF-D01
SF-P02	7,434-8,921 rk	38x89 @600	partition	3579	SF-D02
SF-P03	7,233-8,921 rk	38x89 @600	partition	3629	-
SF-P04	7,233-8,921 rk	38x89 @400	wet room	2262	SF-D03
SF-P05	7,473-8,921 rk	38x89 @400	wet room	2988	-

Length along the wall (mm). Head = top of frame above GF FFL, rk = raked to the rafter soffit less 25 lining, min-max.

DOOR OPENING SCHEDULE

Label	Width	Height	Head	Lintel
SF-D01	846	2100	2100	head rail
SF-D02	846	2100	2100	head rail
SF-D03	810	2100	2100	head rail

Structural opening sizes. Head level above underside of the bottom rail.

PARTITION TIMBER (SECOND FLOOR)

Section	Pieces	Run m	4.8m lengths
38x89 C16	172	249.0	55
18 WBP ply pattress	26	-	-
Slotted partition head clip	35	-	-
47x97 C24 head noggin	32	-	-

From the model. 4.8m lengths = run / 4.8 +5%, not cut-optimised.

NOTES

1. DESIGN ASSUMPTION - internal partitions (TLSTF) read off Offset 9172-SK10 (preliminary): 38x89 C16 studs @600, 38x89 head and bottom rails, 15 plasterboard each side (119); wet-room walls (E-S) at 400 centres with 18 WBP ply pattress in the stud bays, 150-1950 above floor (26 pieces).
2. External walls Nudura 6in XR35 ICF (grey), context only - read with the ICF GAs. SF shown over the ICF below the wall plate (+5,486) and the two front gables. Set-out strings in grey.
3. Room in the roof: EVERY SF partition is RAKED to the rafter soffit less the 25 lining (175 rafters, 45 deg; crown underside +8,946) - schedule HEAD = top of frame min - max above GF FFL. Heads restrained with galv slotted head clips to the rafters / ceiling joists (35 No.) and 47x97 C24 noggins between the rafter pair where a wall runs parallel (32 No.) - clip product to confirm.
4. Sole plates fixed through the SF deck (22 Egger Protect P5, FFL +5,911) to the PS10 joists / noggins at <= 600 c/c. Door openings are structural opening sizes. Check all dimensions on site.
5. OPEN ITEM 1 (red flag): SF-D03 (E-S door in SF-P04): the raked head is only ~129 above the 2,100 door head at the low (west) jamb - head rail + cripple barely fit; confirm the door height / head detail (or shift the door east).

REVISIONS

REV	DATE	DESCRIPTION
-	02.11.26	Quotation issue

Nudura™ BuildEase

CLIENT	PROJECT
ICF Supplies Ltd (distributor) - Tom Barrett	Plot 1, The Rectory, Bates Hill, Ightham TN15 9BG

DRAWING TITLE

SECOND FLOOR TIMBER PARTITIONS

Internal stud partitions, panels and door openings

SCALE	SIZE	DATE
1:75	A3	02.11.26
DRAWN	CHECKED	APPROVED
TS		

STATUS	DRAWING No.	REV
QUOTATION	ES26-075-TF-03	-
