Delivery 1 - Load 1 of 1 - Artic 13.6 m

7 pallets in 4 of 5 floor positions | 152 forms | tallest column 2357 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

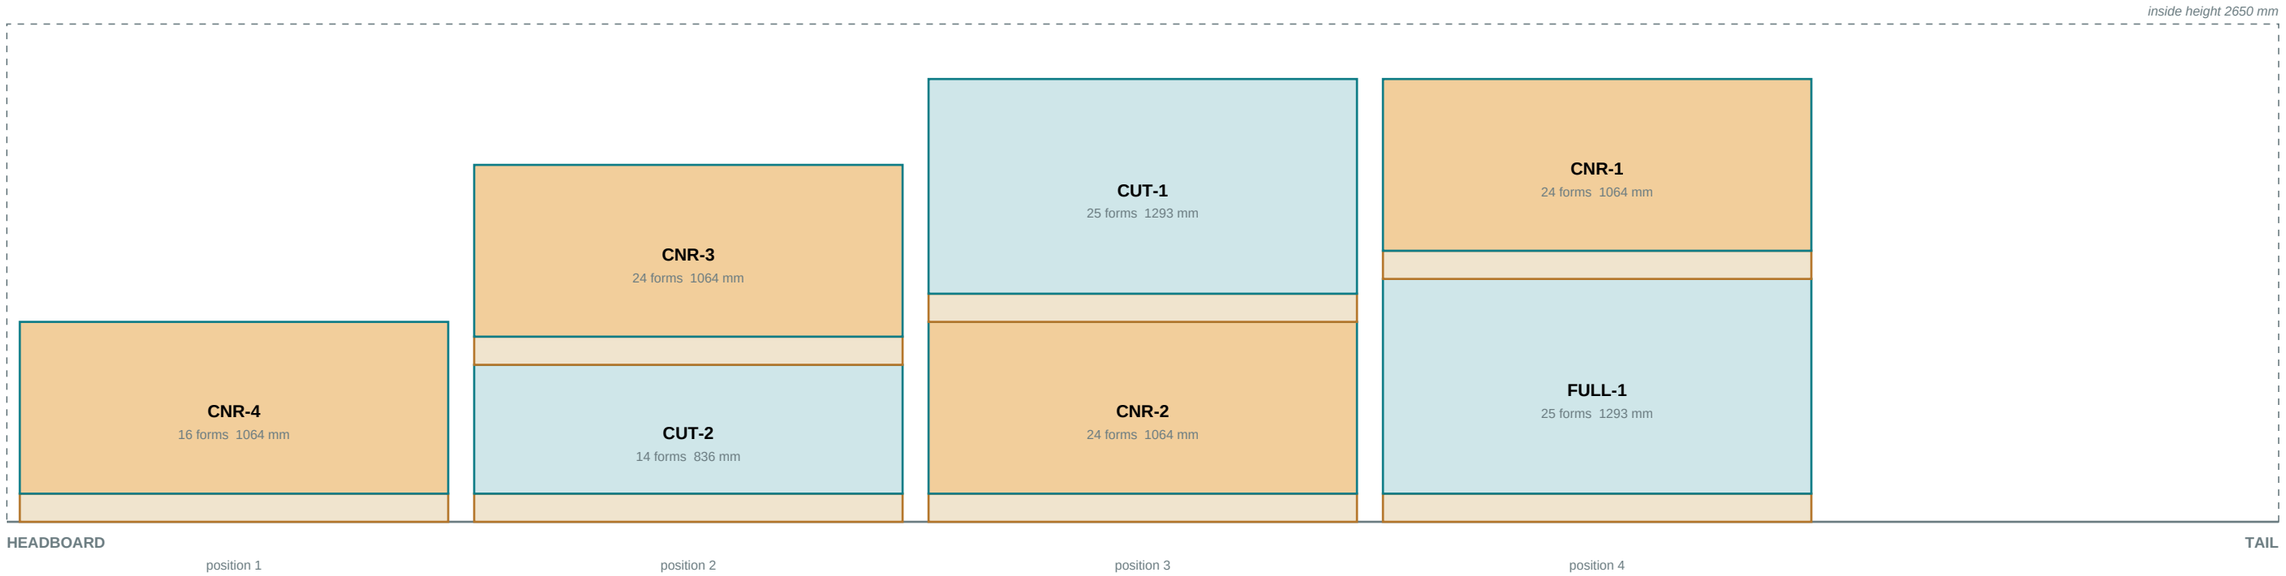

Unload order - 6 of 6 pallets come off out of build order, the price of stacking tallest forward

1. CNR-1 6in XR35 corners 24 forms courses L1 courses 1-2
2. FULL-1 6in XR35 straights 25 forms courses L1 courses 1-5
3. CUT-1 6in XR35 straights 25 forms courses L1 courses 1-6
4. CNR-2 6in XR35 corners 24 forms courses L1 courses 2-4
5. CNR-3 6in XR35 corners 24 forms courses L1 courses 4-6
6. CUT-2 6in XR35 straights 14 forms courses L1 courses 4, 6
7. CNR-4 6in XR35 corners 16 forms courses L1 course 6

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-075 ICF Supplies - Plot 1 The Rectory, I…	FORMS	152
VEHICLE	Artic 13.6 m	POSITIONS	4 of 5
PALLETS	7	TALLEST	2357 mm

Delivery 2 - Load 1 of 1 - Artic 13.6 m

10 pallets in 5 of 5 floor positions | 178 forms | tallest column 2357 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

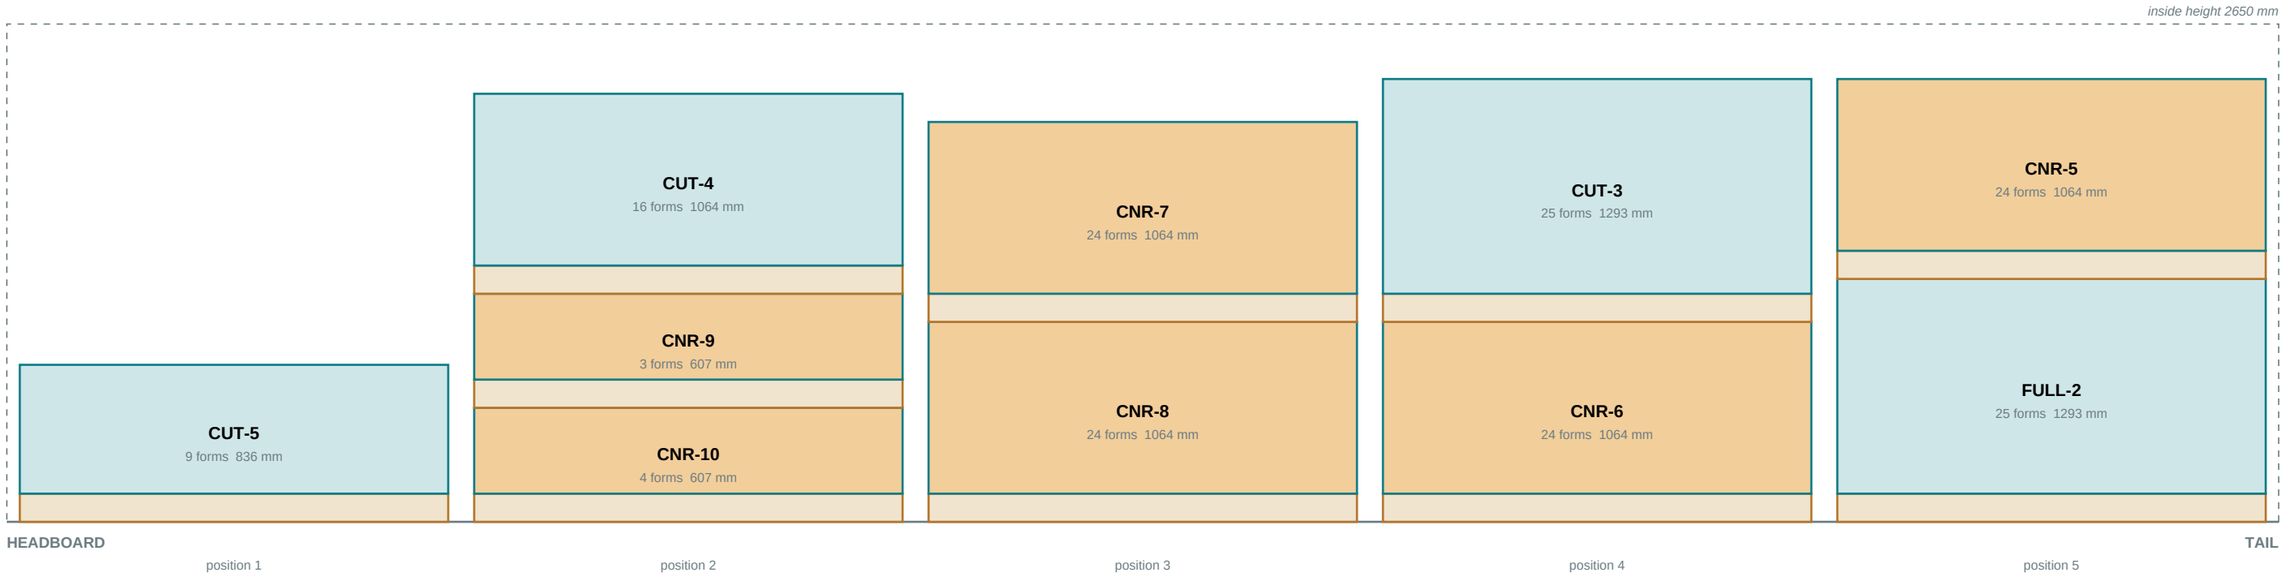

Unload order - 9 of 9 pallets come off out of build order, the price of stacking tallest forward

1. CNR-5 6in XR35 corners 24 forms courses L2 courses 1-2
2. FULL-2 6in XR35 straights 25 forms courses L2 courses 1-3
3. CUT-3 6in XR35 straights 25 forms courses L2 courses 1-6
4. CNR-6 6in XR35 corners 24 forms courses L2 courses 2-3
5. CNR-7 6in XR35 corners 24 forms courses L2 courses 3-5
6. CNR-8 6in XR35 corners 24 forms courses L2 courses 5-6
7. CUT-4 6in XR35 straights 16 forms courses L2 courses 5-6
8. CNR-9 6in XR35 corners 3 forms courses L2 course 6
9. CNR-10 6in XR35 corners 4 forms courses L3 course 1
10. CUT-5 6in XR35 straights 9 forms courses L3 courses 1-4

Nudura™ **WAGON STACKING PLAN** **D2 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-075 ICF Supplies - Plot 1 The Rectory, I…	FORMS	178
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	10	TALLEST	2357 mm
